EAST STROUDSBURG ELEMENTARY SCHOOL
EAST STROUDSBURG AREA SCHOOL DISTRICT

OVERALL PROJECT SCHEDULE

ID	What	Start	Finish	Predecessors
1	**Client Kick-off Meeting**	**Wed 10/19/05**	**Wed 10/19/05**	
2	**TRAFFIC STUDY**	**Mon 12/12/05**	**Fri 7/14/06**	
6	**ZONING HEIGHT VARIANCE**	**Fri 12/9/05**	**Tue 2/7/06**	
11	**SUBDIVISION**	**Fri 2/3/06**	**Tue 3/28/06**	
15	**LAND DEVELOPMENT**	**Tue 11/22/05**	**Tue 10/31/06**	
16	Preliminary drawings developed	Tue 11/22/05	Thu 12/8/05	
17	Sketch Plan Submission	Fri 12/9/05	Tue 12/20/05	16
18	Planning Commission Meeting	Wed 12/21/05	Wed 12/21/05	17
19	Develop LD drawings	Thu 12/22/05	Thu 3/23/06	18
20	Prelim/Final Land Development Submission	Fri 3/24/06	Tue 4/4/06	19
21	Planning Commission Meeting	Wed 4/5/06	Wed 4/5/06	20
22	Conditional Use Hearing	Tue 5/9/06	Tue 5/9/06	
23	Supervisors Approval of Conditional Use	Tue 6/13/06	Tue 6/13/06	
24	Revise Land Final LD drawings	Thu 4/6/06	Thu 5/25/06	
25	Land Development Submission	Fri 5/26/06	Tue 6/6/06	24
26	Planning Commission Meeting	Wed 6/7/06	Wed 6/7/06	25
27	Final Land Development Submission	Wed 6/7/06	Fri 6/23/06	
28	Planning Commission Meeting Cancelled	Wed 7/5/06	Wed 7/5/06	
29	Board of Supervisors Mg Cancelled	Tue 7/11/06	Tue 7/11/06	
30	Submit E/S to Conservation District	Fri 3/3/06	Fri 6/2/06	
31	Resubmit Land Development	Mon 6/26/06	Fri 7/21/06	
32	ReSubmit E/S to Conservation District	Fri 7/21/06	Fri 7/21/06	
33	Planning Commission Meeting - LD	Wed 8/2/06	Wed 8/2/06	
34	Township Supervisor Meeting - LD Approval	Wed 8/9/06	Wed 8/9/06	33
35	Conservation District NPDES Approval	Fri 8/25/06	Fri 8/25/06	34
36	1st Submission of HOP to PennDOT	Fri 3/3/06	Fri 7/21/06	
37	Redesign for PennDOT review comments	Mon 7/24/06	Wed 8/16/06	36
38	2nd Submission for HOP	Thu 8/17/06	Fri 8/18/06	37
39	HOP Approval by PennDOT	Mon 8/21/06	Tue 10/31/06	38
40	Township Meeting Revised Sewer	Wed 10/4/06	Mon 10/9/06	
41	Plan Resubmission, Water, Sewer, MCCD	Mon 10/9/06	Wed 10/25/06	
42	**STUDY PHASE**	**Mon 10/10/05**	**Mon 11/21/05**	
45	**PRE DESIGN PHASE**	**Tue 11/22/05**	**Thu 12/22/05**	
48	**SCHEMATIC DESIGN PHASE**	**Tue 12/20/05**	**Fri 2/24/06**	
52	**DESIGN DEVELOPMENT PHASE**	**Tue 1/24/06**	**Mon 5/1/06**	
64	**CONSTRUCTION DOCUMENTS PHASE**	**Tue 5/2/06**	**Fri 8/25/06**	
73	**BIDDING PHASE**	**Mon 8/28/06**	**Fri 2/23/07**	**72**
74	Advertise	Mon 8/28/06	Fri 9/29/06	
75	PDE PlanCon F Conference Call	Fri 9/22/06	Fri 9/22/06	
76	Prebid Meeting	Mon 9/25/06	Mon 9/25/06	75
77	**Receive Bids**	Wed 10/4/06	Wed 11/1/06	76
78	Owner Approval of Bids	Mon 11/20/06	Mon 12/18/06	77
79	Owner Awards Contracts	Tue 12/19/06	Fri 2/23/07	29,39,78
80	Plancon G Approval	Mon 12/18/06	Mon 1/22/07	
81	Penndot HOP Right of Way Approvals	Mon 8/28/06	Tue 2/6/07	
82	**Contracts Signed and Approved**	Fri 2/23/07	Fri 2/23/07	
83	**CONSTRUCTION PHASE**	**Mon 2/26/07**	**Wed 8/6/08**	
84	Notice To Proceed	Mon 2/26/07	Mon 2/26/07	
85	Mobilize	Mon 2/26/07	Tue 3/13/07	
86	Excavation	Mon 4/30/07	Fri 6/29/07	85
87	Construction	Tue 2/27/07	Wed 8/6/08	
88	**OWNER OCCUPANCY**	Thu 8/7/08	Thu 8/28/08	87

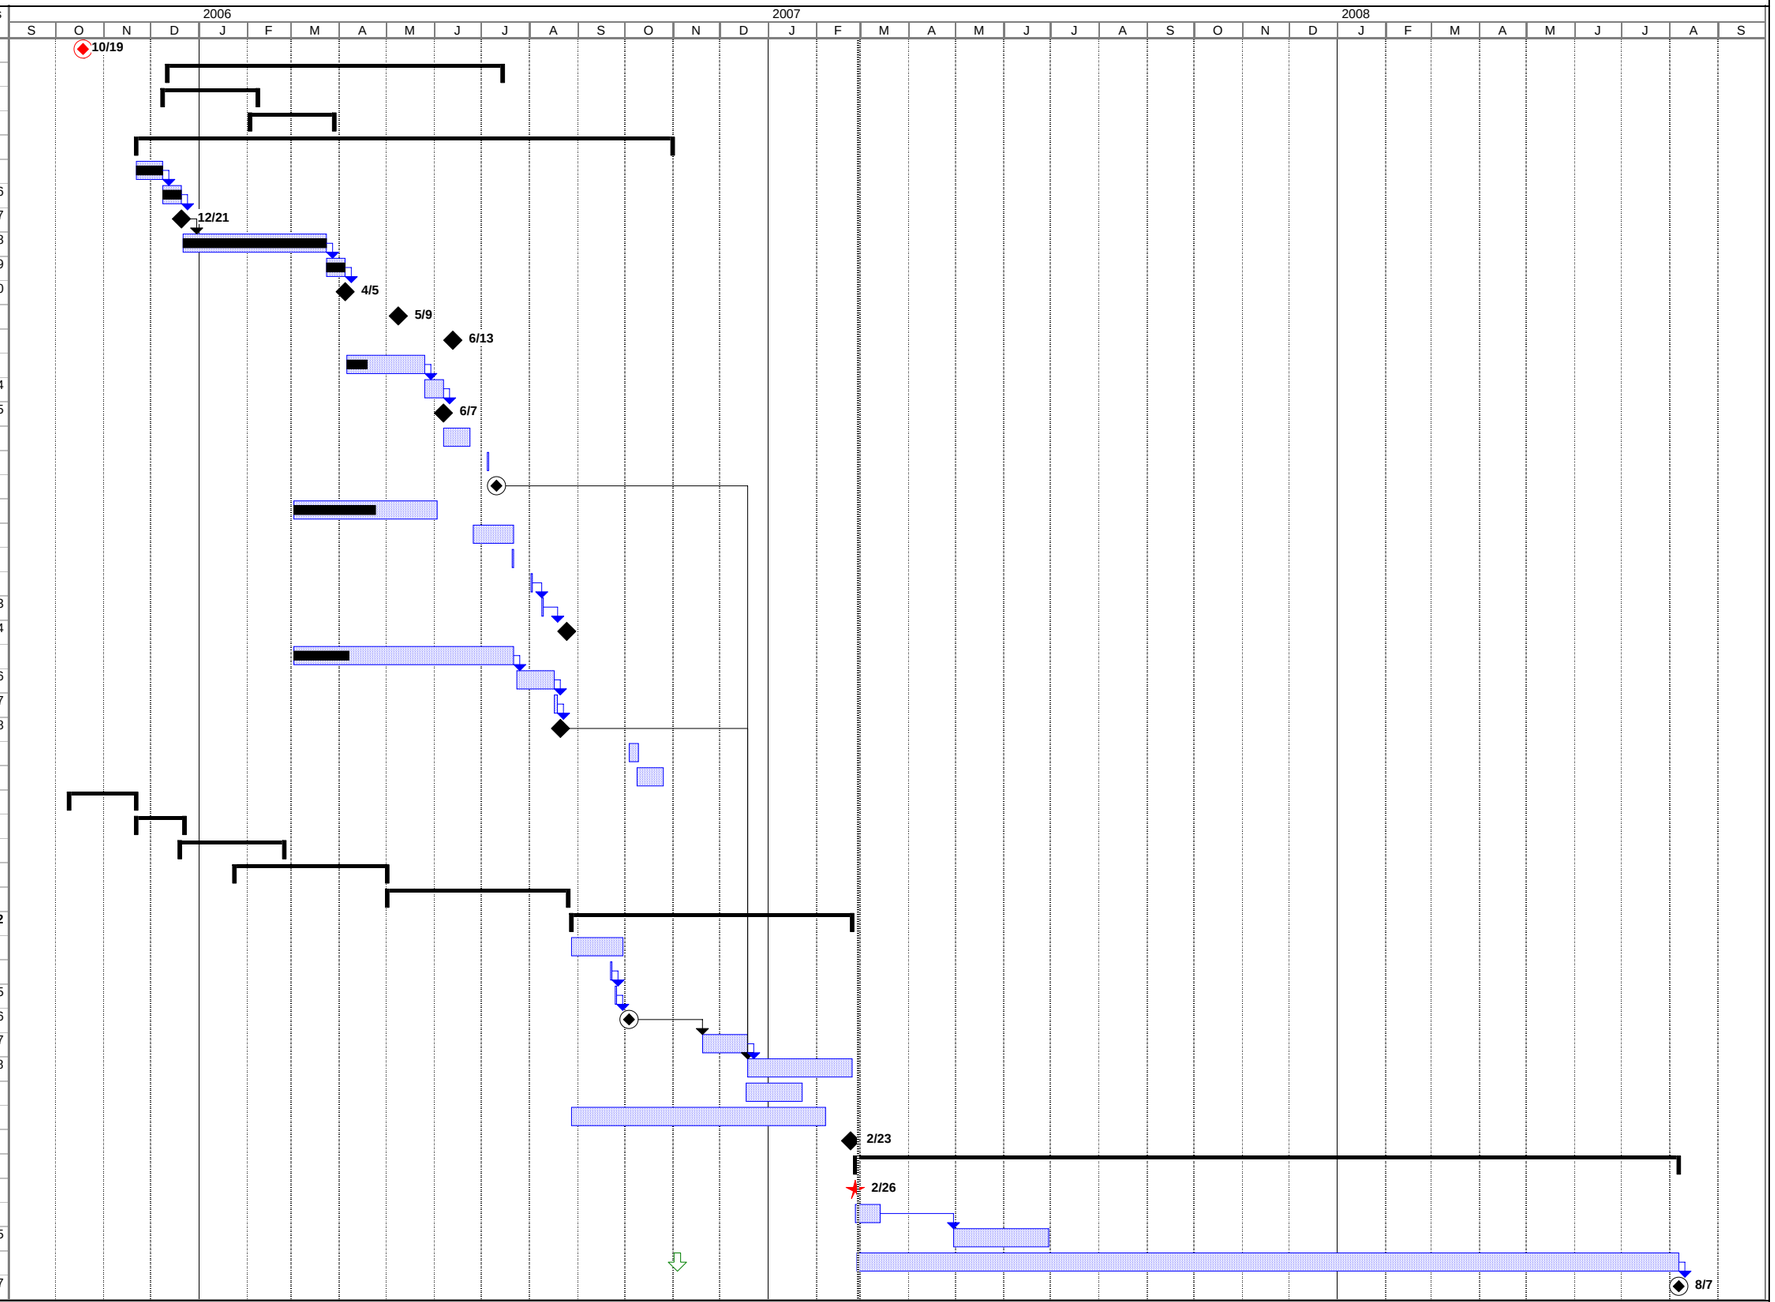

East Stroudsburg Elementary School
Updated: February 27, 2007 - NTP Issued

BUCHART HORN, INC. / BASCO ASSOCIATES
