Activity Description	Early Finish	Total Float
MILESTONE		
CMPL PH S2: BRIDGE	NOV 29 06A	
CMPL PH S1: BUILDING P & SITE	MAY 24 07	-39
CMPL PH S9: FIELDHOUSE SOUTH SITEWORK	MAY 24 07	70
CMPL PH S3: PARKING LOTS & TEMPORARY EXITS		
CMPL PH S8: STADIUM, PARKING LOTS, DRIVEWAY	MAY 25 07	67
CMPL PH S6A: PARKING LOTS/STORMWATER/UTILITIES		
CMPL PH S7: BASEBALL FIELD & TENNIS COURTS	JUN 01 07	-55
CMPL PH S6B: PARKING LOTS/STORMWATER/UTILITIES	JUN 15 07	-33
CMPL PH S5: FIELDHOUSE ADDITION & ELEC SERVICE	JUN 26 07	429
COMPLETE PHASE R1	JUL 23 07	30
CMPL PH S11: N COURTLAND STREET	AUG 10 07	44
CMPL PH S10: BUS LOOP	AUG 13 07	4
CMPL PH R2: UNIT E & GALLERY LIBRARY	AUG 30 07	0
CMPL PH R3: NURSE'S SUITE	OCT 18 07	-3
CMPL PH N1A: UNIT C&D - CAFETERIA/THEATER/MUSIC	NOV 15 07	-52
CMPL PH N1: UNIT B&C - CLASSROOM ADDITION	DEC 24 07	-36
CMPL PH N2A - SCIENCE/GREENHOUSE ADDITION	DEC 31 07	0
CMPL PH R4: ADMIN, CLASSROOMS & AUDITORIUM	APR 30 08	0
CMPL PH N2: UNIT K - GYMNASIUM ADDITION	AUG 22 08	6
CMPL PH S13: DEMO N COURTLAND BUILDING	AUG 28 08	129
CMPL PH R5: BUSINESS CLASSROOMS	AUG 29 08	1
CMPL PH S12: DEMO BUNNELL BUILDING	SEP 22 08	29
CMPL PH N2B: UNITS H&J - ADMIN ADDITION	NOV 03 08	0
CMPL PH R6: EAST ROOMS	DEC 30 08	1
CMPL PH R7: GYMNASIUM & AUDITORIUM	DEC 30 08	1

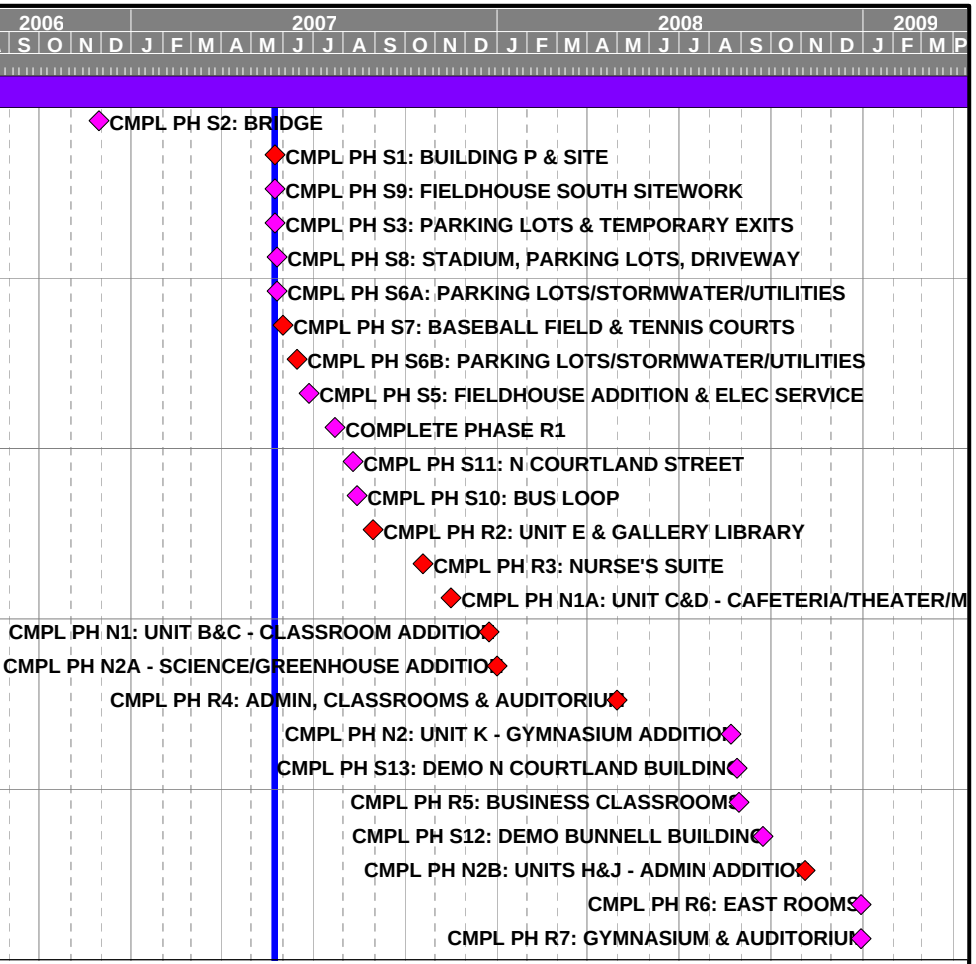

Start Date	JUL 05 06
Finish Date	JAN 28 09
Data Date	MAY 25 07
Run Date	JUN 14 07 15:21

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

ES08 Sheet 1 of 1

BORO CONSTRUCTION INC.

EAST STROUDSBURG HIGH SCHOOL - SOUTH

Milestone Schedule As Of MAY 25 07

Date	Revision	Checked	Approved
